

Infrastructure Projects

**Update to Hutto City Council
February 17, 2022**

Design - 100% plans to TxDOT

Design review meeting – Feb 28

Final design complete Spring 2022

Right of Way acquisition and Utility relocations – 3 offers extended, remaining appraisals in process

Construction award (bid) - Summer 2022

Construction Phase - Start Fall 2022;
complete Summer 2023

Advanced Funding Agreement (AFA)
with TxDOT – awaiting final document



Design – 100% submitted to TxDOT with revised layout (removed US79 turn lane)

Final design complete Spring 2022

Right of Way acquisition – updated appraisal and offer extended

UPRR railroad coordination –
Agreements for Engineering and
Construction required

Construction Phase - Start Fall 2022;
complete Fall 2023

Advanced Funding Agreement (AFA) @
TxDOT – awaiting final document





FM 1660 S at US 79

Design – 60% plans to TxDOT

Final design to include major slope changes to US 79 and FM 1660 South.

Traffic signal design alternatives


Final design complete Fall 2023

Construction award (bid) - Spring 2024

Construction Phase - Start Summer 2024;
complete Summer 2025

Advanced Funding Agreement (AFA) with TxDOT

Railroad (UPRR) – CRISI grant funds awarded;
Site meeting Feb 28

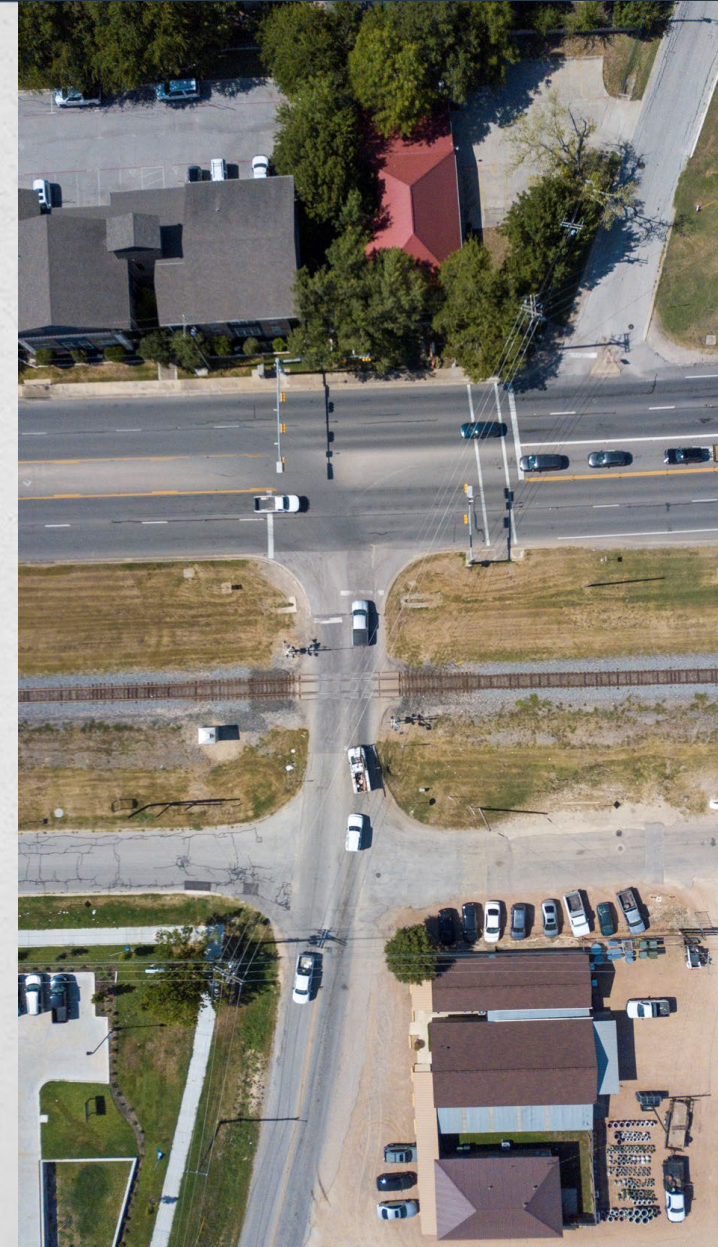

Construction Activity:

Water main pipe installation complete.

Contractor installing service connections and tie-ins. Once complete, will perform disinfection and pressure testing.

Water line completion date – April 2022

Atmos – gas line replacement (West Street to FM 1660) confirmed. Awaiting updated gas construction schedule.

Pavement – evaluating condition of base and asphalt repairs needed



Conceptual design complete

Property owner outreach last week

Design includes:

- Channel slope stabilization

- Add walkable area adjacent to fence

- Improved drainage to detention pond outfall

Bidding and award – Spring 2022

Construction – Summer 2022



Phase One - Approximately 13,000 LF of sidewalk improvements - both sides of street


Estate Drive from Lakemont to Katz

Little Lake Road from Katz to CR 138

Design – Spring 2022

Bidding and award – Summer 2022

Construction – Fall 2022

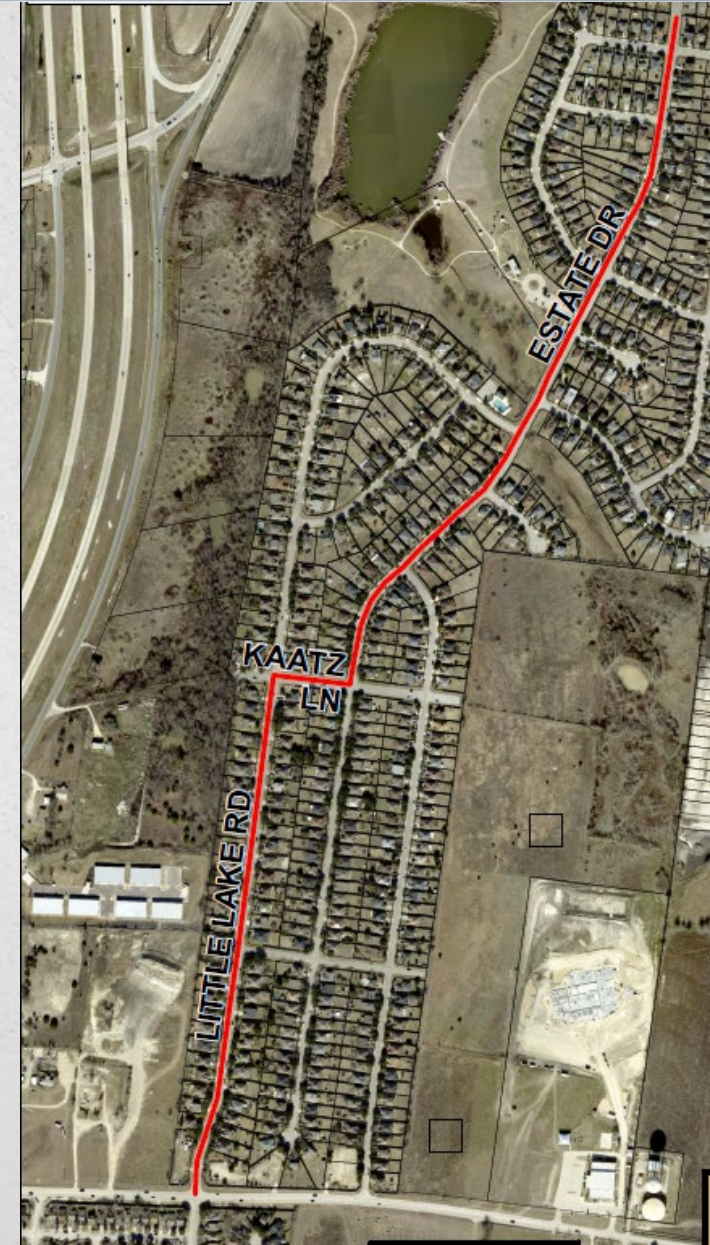

CR 137 – FM 1660 to Brushy Creek

Original scope – mill and overlay existing limits

Scope revised to address traffic and drainage

Revised Scope

- Right Turn Lane on FM 1660 onto CR 137
- Left turn lane on CR 137 at FM 1660
- Upgrade traffic signal
- Improve roadway drainage capacity

Finalize task order and initiate TxDOT coordination

Design – begin Spring 2022

Bidding and award – Summer 2023

Construction – Fall 2023

